



New Women and Babies Hospital Project

Osborne Park Hospital expansion construction update – September 2026

Osborne Park Hospital (OPH) is undergoing a major transformation as part of the landmark New Women and Babies Hospital Project.


What's happening in September?

First structural concrete pour completed

The first structural concrete pour was completed on site earlier this month.

The core three raft slab concrete pour reinforces the foundation, which will support part of the structure, providing the strength and stability needed from the ground up.

The milestone required 130 tonnes of reinforced steel, 500 cubic metres of concrete and 85 concrete trucks, with the pour completed over nine hours.

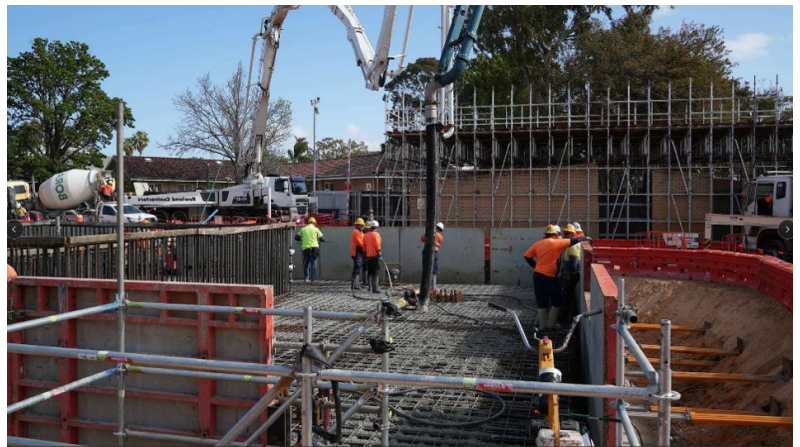

This was the first of several core pours that will occur this month.

Planning for a much larger concrete pour at the site is underway and expected to take place in the coming weeks. Separate out-of-hours works notices, including times and impacts will be provided to stakeholders prior to the concrete pour.

Second of three tower cranes to arrive

The second of three tower cranes has been installed joining the inaugural crane, which arrived in July. Collectively, the tower cranes enable significant structural works to be undertaken. They will be fully electric, producing lower emissions and contributing to a more sustainable construction process.

Construction of temporary road

Work to build a temporary road between Limosa Close and the construction site is nearing completion. The road provides direct and safe site access for construction vehicles during construction hours. The road, which will not be accessible to the public, will be open from mid-September.

Northern car park

Stage 1 works for the new northern car park (adjacent to Osborne Place) will be completed in the middle of September. The works include asphaltting, kerbing, and line marking. Stage 2 works will start immediately following the completion of Stage 1 and will include the installation of new soak wells, which is an underground water drainage system, and supporting services.



Completed works

Sheet piling

Sheet piling is now complete. Sheet piling is a construction technique that involves driving interlocking steel sheets into the ground to hold the soil in place allowing excavation to be undertaken on the other side. The machinery used for these works has now been removed from site.

What to expect from upcoming works

- General construction noise, dust and vibrations. Levels are continuously monitored to remain within safe, industry-approved limits.
- Tower crane horns during critical lifts when ground workers need to be alerted or move out of the way for safety reasons. At other times, two-way radios will be used to limit the noise from the tower cranes.
- Increased traffic and heavy vehicle movements where site works are taking place.
- Traffic management measures, including signage and personnel to assist pedestrians, motorists and cyclists. This may include stop-slow traffic controls and temporary diversions.
- Construction vehicles and equipment, such as survey equipment, compactors and hand tools.
- Lighting and construction activity during scheduled out of hours work. Impacted stakeholders will be notified ahead of these works and lighting will be directed toward the intended target to prevent excessive light spill.
- All impacts will be closely monitored and action taken promptly as needed.

In addition to the Osborne Park Hospital expansion several unrelated residential construction projects are currently underway in the surrounding area.

Plan your visit

If you are visiting the hospital, please plan ahead and allow extra travel time. For more information on where to park, visit the hospital's website at [Osborne Park Hospital - visiting the hospital](#).

There is a hop-on / hop-off buggy service available to pick visitors up onsite at sign posted buggy stops from 8am to 4.30pm Monday to Friday. See [buggy stop map](#) for further details.

Contact

For non-urgent enquiries please contact the New Women and Babies Hospital Project Community Line on (08) 9326 3666 or womenandbabies@omid.wa.gov.au
